


Renew Stations STATUS & MILESTONES

EXPENDED Thru 03/2024: **\$82.8**
 FORECAST Thru 06/2025: **\$107.1**
 TOTAL PROGRAM VALUE: **\$210**
 PERIOD CASHFLOW: **\$3.1**

All values are in millions

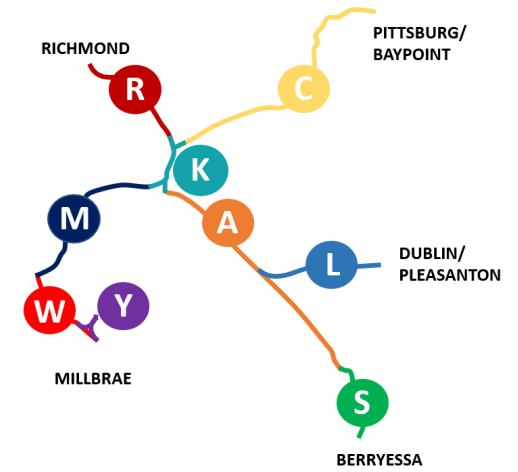

STATUS – Renew Stations

# Projects in Planning	# Projects in Design	# Projects in Bid/Award	# Projects in Construction	# Projects Completed	TOTAL # Projects
0	1	0	2	5	8

MILESTONES

Completed (Jan 2024 – Mar 2024)	Q4 (Apr 2024 – June 2024)	Q1 (Jul 2024 – Sep 2024)	Q2 (Oct 2024 – Dec 2024)
<ul style="list-style-type: none"> Completion of Construction for P3 Platform Escalator at Montgomery St. Station <i>Completion of Construction for Canopy 6 at Embarcadero Station</i> 	<ul style="list-style-type: none"> Completion of Construction for Canopy 2 at Embarcadero Station and Canopy 9 at Montgomery St. Station Completion of Construction for P6 Platform Escalator at Embarcadero Station <i>Completion of Construction for P1 Platform Escalator at Powell St. Station and P4 Platform Escalator at Civic Center Station</i> 	<ul style="list-style-type: none"> Completion of Construction for P1 Platform Escalator at Montgomery St. Station 	<ul style="list-style-type: none"> <i>Completion of Construction for S5 Street Level Escalator at Embarcadero Station</i> <i>Completion of Construction for Canopy 5 at Embarcadero Station</i>

Watchlist:

- Construction of Canopies

Italic: Modified milestones from previous report.

