


Renew Stations STATUS & MILESTONES

EXPENDED Thru 06/2024: **\$83.3**
 FORECAST Thru 06/2025: **\$107.1**
 TOTAL PROGRAM VALUE: **\$210**
 PERIOD CASH FLOW: **\$0.5**

All values are in millions

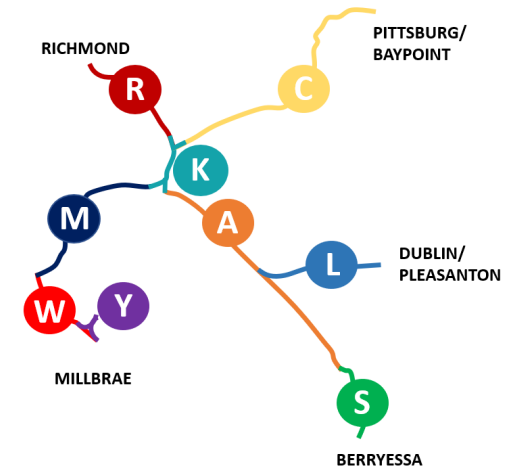

STATUS – Renew Stations

# Projects in Planning	# Projects in Design	# Projects in Bid/Award	# Projects in Construction	# Projects Completed	TOTAL # Projects
1	2	0	2	5	10

MILESTONES

Completed (Apr 2024 – June 2024)	Q1 (Jul 2024 – Sep 2024)	Q2 (Oct 2024 – Dec 2024)	Q3 (Jan 2025 – March 2025)
<ul style="list-style-type: none"> Construction of Canopy 2 at Embarcadero Station and Canopy 9 at Montgomery St. Station Construction of P6 Platform Escalator at Embarcadero Station Construction of P1 Platform Escalator at Powell St. Station and P4 Platform Escalator at Civic Center Station 	<ul style="list-style-type: none"> Completion of Construction for P1 Platform Escalator at Montgomery St. Station <i>Completion of Construction for Canopy 5 at Embarcadero Station</i> 	<ul style="list-style-type: none"> Completion of Construction for S5 Street Level Escalator at Embarcadero Station 	<ul style="list-style-type: none"> <i>Completion of Construction for P2 Platform Escalator at Civic Center Station, P3 Platform Escalator at Embarcadero Station, and P5 Platform Escalator at Powell St. Station</i> <i>Completion of Construction for Canopy 7 at Montgomery Station and Canopy 18 at Civic Center Station</i>

Watchlist:

- Construction of Canopies

Italic: Newly added and modified milestones from previous report.

