


# Station Access STATUS & MILESTONES

EXPENDED Thru 06/2024: \$45.4  
 FORECAST Thru 06/2025: \$69.2  
 TOTAL PROGRAM VALUE: \$135  
 PERIOD CASHFLOW: \$1.9  
*All values are in millions*

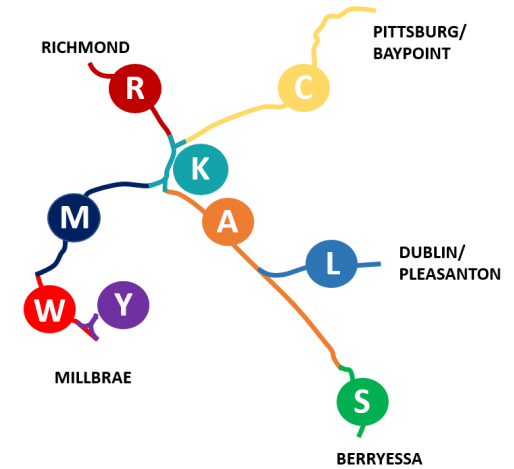

## STATUS – Expand Safe Access to Stations

# Projects in Planning	# Projects in Design	# Projects in Bid/Award	# Projects in Construction	# Projects Completed	TOTAL # Projects
3	9	3	7	13	35

MILESTONES			
Completed (Apr 2024 – June 2024)	Q1 (Jul 2024 – Sep 2024)	Q2 (Oct 2024 – Dec 2024)	Q3 (Jan 2025 – March 2025)
<ul style="list-style-type: none"> <li>Began Demolition for ADA Access Corrections at Castro Valley Station</li> <li><i>Construction of Stairway Bicycle Channels at 12th Street Station</i></li> </ul>	<ul style="list-style-type: none"> <li>Completion of Design for the Dublin/Pleasanton Access Improvement Project</li> <li><i>Begin Exterior Construction for ADA Access Corrections at Castro Valley, San Leandro, Fruitvale, Rockridge, and Richmond Stations</i></li> <li><i>Completion of Construction of Stairway Bicycle Channels at Walnut Creek Station</i></li> <li><i>Completion of Construction of SR2B-funded Iron Horse Trail Bridge Project</i></li> </ul>	<ul style="list-style-type: none"> <li>Completion of Design for Pittsburg/Bay Point Shared Mobility Improvement Project</li> <li>Completion of Construction of Stairway Bicycle Channels at Civic Center, Embarcadero, and 24th St. Stations</li> <li><i>Completion of Exterior Construction for ADA Access Corrections at Castro Valley, Rockridge, and Richmond Stations</i></li> </ul>	<ul style="list-style-type: none"> <li><i>Contract Award for PA System Improvement</i></li> <li><i>Issue for Bid Dublin/Pleasanton Station Access Improvements</i></li> </ul>

### Watchlist:

- City of Pittsburg BART Ped/Bike Connectivity Project Construction

\*Milestone for 19<sup>th</sup> Street Access Improvement Project (Bike Station) removed due to project on hold

*Italic: Newly added and modified milestones from previous report.*

