


# Renew Stations STATUS & MILESTONES

EXPENDED Thru 09/2024: \$89.3  
 TOTAL PROGRAM VALUE: \$210  
 PERIOD CASH FLOW: \$6.0  
*All dollar values are in millions*

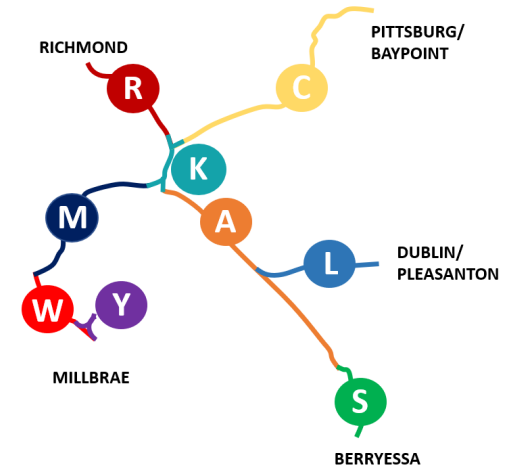

## STATUS – Renew Stations

# Projects in Planning	# Projects in Design	# Projects in Bid/Award	# Projects in Construction	# Projects Completed	TOTAL # Projects
1	2	0	2	5	10

MILESTONES			
Completed (Jul 2024 – Sep 2024)	Q2 (Oct 2024 – Dec 2024)	Q3 (Jan 2025 – March 2025)	Q4 (Apr 2025 – June 2025)
<ul style="list-style-type: none"> <li>Completed Construction for P1 Platform Escalator at Montgomery St. Station</li> <li>Completed Construction for Canopy 5 at Embarcadero Station</li> </ul>	<ul style="list-style-type: none"> <li>Completion of Construction for S5 Street Level Escalator at Embarcadero Station</li> </ul>	<ul style="list-style-type: none"> <li>Completion of Construction for P2 Platform Escalator at Civic Center Station, P3 Platform Escalator at Embarcadero Station, and P5 Platform Escalator at Powell St. Station</li> <li>Completion of Construction for Canopy 7 at Montgomery Station and Canopy 18 at Civic Center Station</li> <li><i>Completion of Construction for Canopy 1 at Embarcadero Station</i></li> </ul>	<ul style="list-style-type: none"> <li><i>Issue for Bid for Embarcadero Station Platform Elevator</i></li> <li><i>Completion of Construction for Canopies 10 and 17 at Market Street Station</i></li> </ul>

### Watchlist:

- Construction of Canopies

*Italic: Newly added and modified milestones from previous report.*

