


# Tunnels & Structures

## STATUS & MILESTONES

EXPENDED Thru 09/2024: **\$264.1**  
 TOTAL PROGRAM VALUE: **\$549**  
 PERIOD CASHFLOW: **\$5.7**  
*All dollar values are in millions*

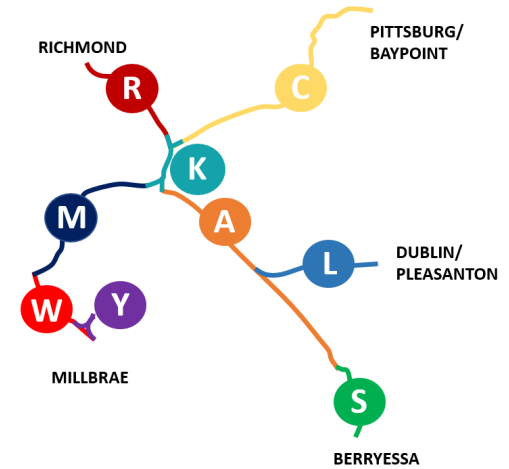

### STATUS – Repair Tunnels & Structures

# Projects in Planning	# Projects in Design	# Projects in Bid/Award	# Projects in Construction	# Projects Completed	TOTAL # Projects
0	2	6	7	12	27

MILESTONES			
Completed (Jul 2024 – Sep 2024)	Q2 (Oct 2024 – Dec 2024)	Q3 (Jan 2025 – March 2025)	Q4 (Apr 2025 – June 2025)
<ul style="list-style-type: none"> <li>Completed Construction (In-house) of Renew Catwalks at Aerial Structure (Phase 3A)</li> </ul>	<ul style="list-style-type: none"> <li>Completion of Design for Richmond Yard Carwash Building Fence</li> <li>Completion of Aerial Bearing Pad Assessment</li> </ul>	<ul style="list-style-type: none"> <li>Begin Construction for Water Intrusion at Train Control Rooms (Package 2, 4 locations)</li> </ul>	<ul style="list-style-type: none"> <li><i>Completion of Construction (In-house) of Renew Catwalks at Aerial Structure (Phase 3B)</i></li> </ul>

### Watchlist:

- Design for Water Intrusion at Train Control Rooms

*Italic: Newly added and modified milestones from previous report.*

