


Station Access STATUS & MILESTONES

EXPENDED Thru 09/2024: \$46.5
 TOTAL PROGRAM VALUE: \$135
 PERIOD CASHFLOW: \$1.1
All dollar values are in millions

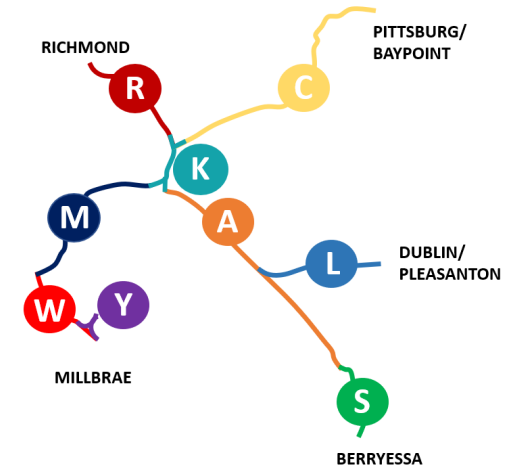

STATUS – Expand Safe Access to Stations

# Projects in Planning	# Projects in Design	# Projects in Bid/Award	# Projects in Construction	# Projects Completed	TOTAL # Projects
3	9	3	7	13	35

MILESTONES			
Completed (Jul 2024 – Sep 2024)	Q2 (Oct 2024 – Dec 2024)	Q3 (Jan 2025 – March 2025)	Q4 (Apr 2025 – June 2025)
<ul style="list-style-type: none"> Completed Design for the Dublin /Pleasanton Access Improvement Project Began Exterior Construction for ADA Access Corrections at Castro Valley, San Leandro, Fruitvale, Rockridge, and Richmond Stations Completed Construction of Stairway Bicycle Channels at Walnut Creek Station 	<ul style="list-style-type: none"> Completion of Design for Pittsburg/Bay Point Shared Mobility Improvement Project Completion of Construction of Stairway Bicycle Channels at Civic Center, Embarcadero, and 24th St. Stations Completion of Exterior Construction for ADA Access Corrections at Castro Valley, Rockridge, and Richmond Stations <i>Completion of Construction of SR2B-funded Iron Horse Trail Bridge Project</i> 	<ul style="list-style-type: none"> Contract Award for PA System Improvement <i>Completion of North Berkeley Active Access Project</i> 	<ul style="list-style-type: none"> <i>Issue for Bid Dublin/Pleasanton Station Access Improvements</i>

Watchlist:

- City of Pittsburg BART Ped/Bike Connectivity Project Construction

Italic: Newly added and modified milestones from previous report.

